

Fox Point-Bayside Construction Update

Provided by Miron Construction Co., Inc.



APRIL 2024 | PROGRESS SUMMARY

Our construction projects at Bayside Middle and Stormonth Elementary are continuing to progress. Here is what has been happening:


Bayside Middle School

Happening Now

- Gym – Painting of the gym continues this month.
- New District Office – Drywall and finishing have begun.
- Commons Area – Concrete slabs have been poured in the commons space and music rooms.
- Classrooms – Painting continues in the classrooms and cabinets are being installed. Installation of ceiling grid and lights has also begun.

Looking Ahead

- Gym – Painting continues in preparation for installation of lights and gym equipment.
- New District Office – Drywall and finishing continue. Painting will begin in April.
- Commons – Wall framing and drywall will be completed in April. Mechanical and electrical systems are ongoing.
- Classrooms – Ceramic tile in the bathrooms is being installed. Flooring and carpet installation will start in April.

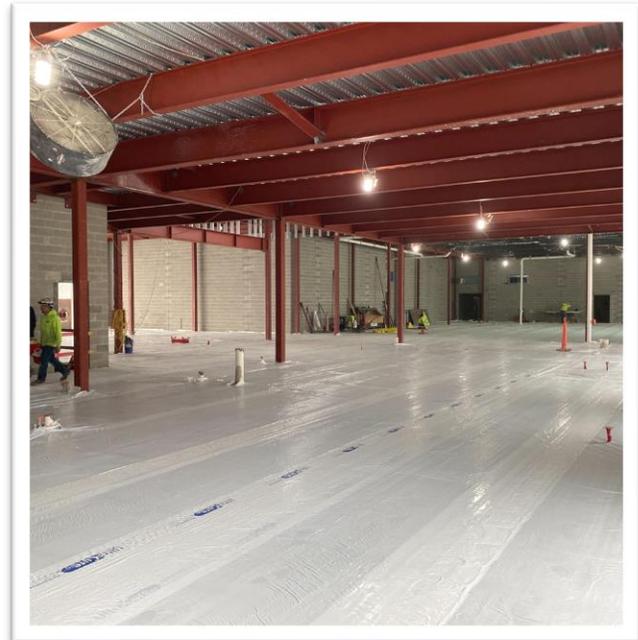

Concrete slabs were poured in the Commons Area.



Preview of what the new classroom spaces will look like (finishes continue to be installed).



Metal panels are finalizing the exterior façade.

Construction Questions? Contact Josh Brzezinski | Project Superintendent | Bayside MS | 920-843-2830

Fox Point-Bayside Construction Update

Provided by Miron Construction Co., Inc.




Stormonth Elementary School

Happening Now


- Former District Office (New Conference Rooms) – Framing of the new walls are complete, mechanical and electrical rough-ins continue.
- Basement and Attic – Fire alarm and sprinkler rough-ins have begun.
- Locker Rooms – Demolition and plumbing rough-ins started over spring break.

Looking Ahead


- New Conference Rooms – Drywall installation begins next week.
- Basement and Attic – Fire alarm and sprinkler installation continue.
- Locker Rooms – Floor leveling to begin after demolition is complete.

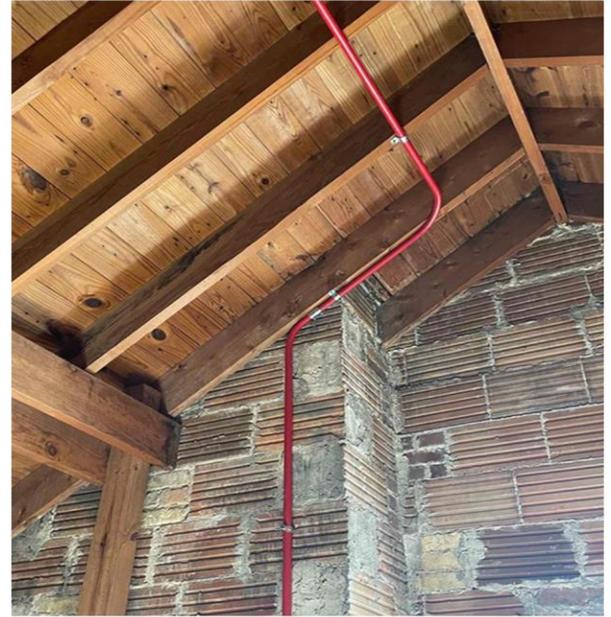

The sprinkler system is being installed in the attic.

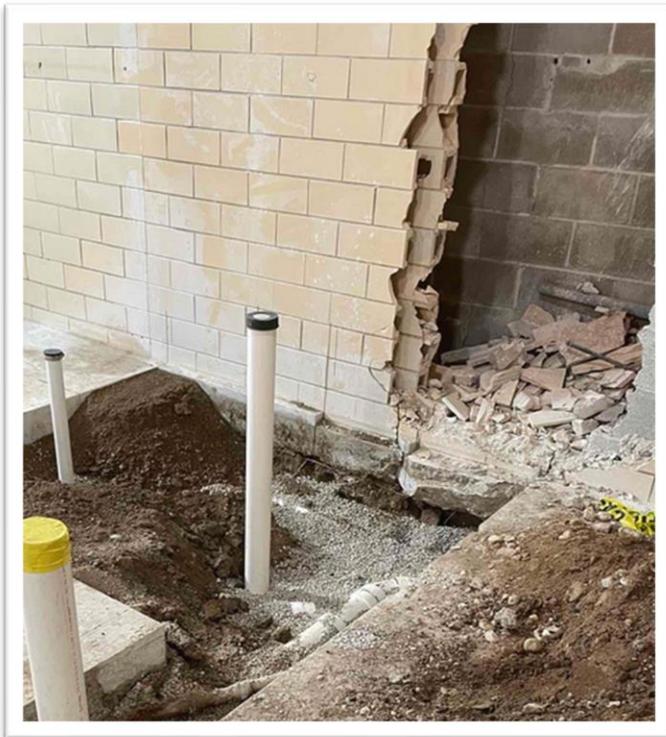

Demolition in the locker room for new plumbing rough-ins.

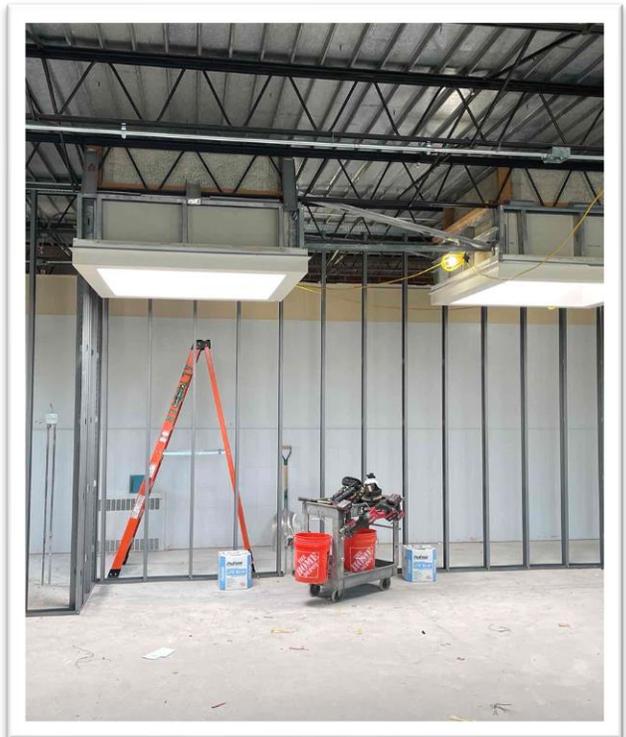

Walls are being constructed in the new conference rooms.

Construction Questions?

Contact Tin Truong | Project Superintendent | Stormonth ES | 920-279-4458

