

# Fox Point-Bayside Construction Update

Provided by Miron Construction Co., Inc.



## OCTOBER 2023 | Progress Summary

Welcome back to school! We're excited to see students and staff on campus. Our construction projects at Bayside Middle School and Stormonth Elementary are progressing in the following areas:

- Gym - Concrete masonry walls are complete on the west and north elevations.
- District Office - Concrete foundations and steel column pads are complete.
- Concrete footings and foundations are nearing completion. The band, choir, and orchestra areas are complete and foundations for the new LMC will be complete by mid-October.
- Classroom stair towers and structural steel framing and decking will be complete by mid-October.
- Stormonth - attic windows completed by November.



Bayside gym wall installation



Stormonth received new energy efficient windows



Stormonth had 230 new windows installed

# Fox Point-Bayside Construction Update


Provided by Miron Construction Co., Inc.



## Looking Ahead

- Gym/District Office - Concrete masonry walls for the gym and stage will be completed by mid-October. Structural steel framing and roof joists will follow.

- Masonry walls for the band/choir/orchestra areas will begin in mid-October and go into November.
- Classroom exterior envelope construction (walls and roofing) will begin mid-October.

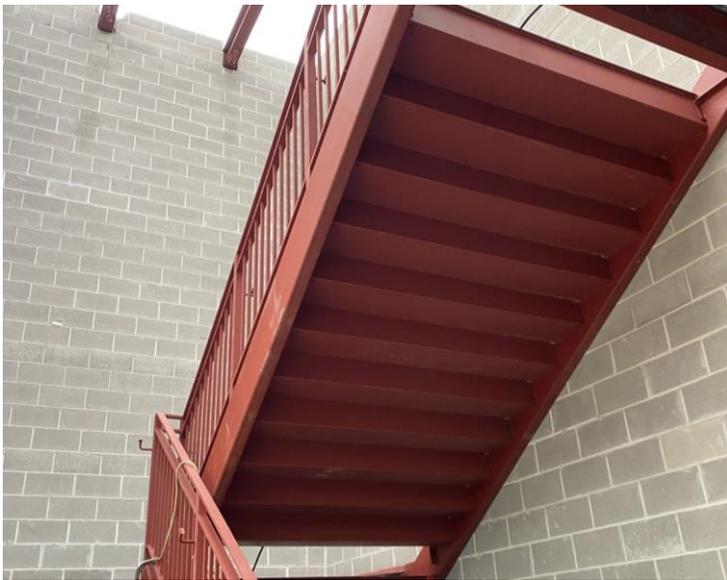

Classroom stair tower and steel framings on SW corner



Steel stairs installed to the second-floor classrooms



Structural steel for two-story classroom wing and roof



New gym masonry walls

**Construction Questions?** Contact Josh Brzezinski | Project Superintendent | 920-843-2830

